[IoT Operation monitoring IoT for JTEKT] Project Schedule

[JTEKT AUTOMOTIVE (THAILAND) CO.,LTD.]

Copyright© TOMAS TECH CORPORATION. All rights reserved.

Project Start Date: Mon 13-11-23
Project Lead: Thu 30-11-23
Display Week: 1
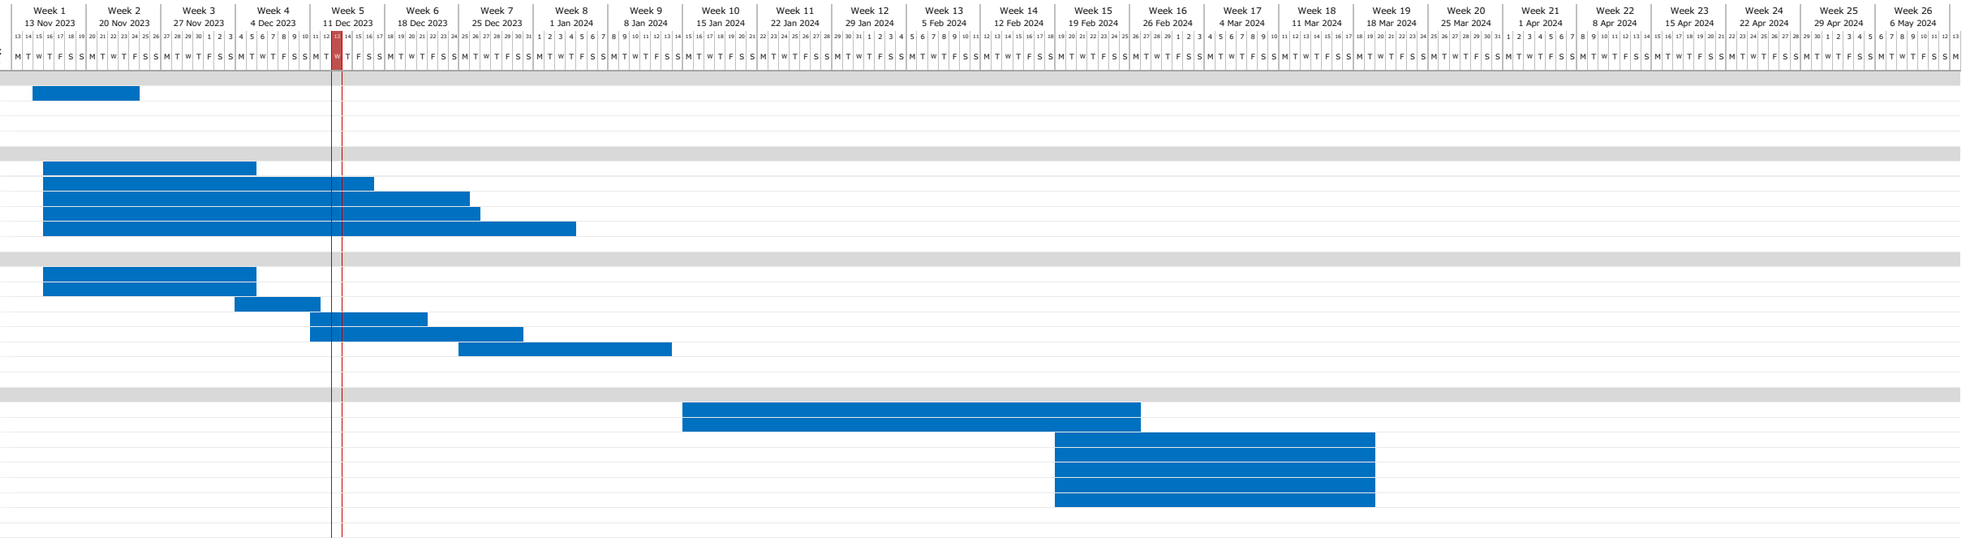
WBS	TASK	PIC	START	END	DAYS	% DONE	WORK DAYS
1	**Kick-off meeting**			-			-
1.1	Kick-off meeting after PO	JATH/Tomas	Wed 15-11-23	Fri 24-11-23	10	0%	8
1.2				-			-
1.3				-			-
1.4				-			-
2	**Software schedule**			-			-
2.1	Requirements confirmation	JATH/Tomas	Thu 16-11-23	Tue 05-12-23	20	0%	14
2.2	Data organization/confirmation	JATH/Tomas	Thu 16-11-23	Sat 16-12-23	31	0%	22
2.3	System Design	Tomas	Thu 16-11-23	Mon 25-12-23	40	0%	28
2.4	Software development	Tomas	Thu 16-11-23	Tue 26-12-23	41	0%	29
2.5	Software test	Tomas	Thu 16-11-23	Thu 04-01-24	50	0%	36
2.6							-
3	**Hardware schedule**			-			-
3.1	Requirements and site survey confirmation	JATH/Tomas	Thu 16-11-23	Tue 05-12-23	20	0%	14
3.2	System Design	Tomas	Thu 16-11-23	Tue 05-12-23	20	0%	14
3.3	Drawing Desgin	Tomas	Mon 04-12-23	Mon 11-12-23	8	0%	6
3.4	Hardware procurement	Tomas	Mon 11-12-23	Thu 21-12-23	11	0%	9
3.5	Hardware pre-shipment confirmation	Tomas	Mon 11-12-23	Sat 30-12-23	20	0%	15
3.6	Hardware Assembly	Tomas	Mon 25-12-23	Sat 13-01-24	20	0%	15
3.7				-			-
3.8				-			-
4	**Installation**			-			-
4.1	Software installation	Tomas	Mon 15-01-24	Mon 26-02-24	43	0%	31
4.2	Hardware installation and wiring	Tomas	Mon 15-01-24	Mon 26-02-24	43	0%	31
4.3	Teaching for UT	JATH/Tomas	Mon 19-02-24	Tue 19-03-24	30	0%	22
4.4	User Testing & Trial	JATH/Tomas	Mon 19-02-24	Tue 19-03-24	30	0%	22
4.5	Supports user feedback	JATH/Tomas	Mon 19-02-24	Tue 19-03-24	30	0%	22
4.6	Teaching for Go live	JATH/Tomas	Mon 19-02-24	Tue 19-03-24	30	0%	22
4.7	Go live	JATH/Tomas	Mon 19-02-24	Tue 19-03-24	30	0%	22
4.8				-			-
4.9							-
